


Waterfall Plan: Ledger — School Event Register

CSPC1 • Topic 2 Lab Activity: Waterfall Plan for Your Group Project • Project repo:
github.com/HimawariCatty/Ledger-School-Event-Register • 9-week plan, 5 phases

Deliverable 1. Gantt Chart

Ledger — School Event Register: Waterfall Gantt Chart (9 Weeks)

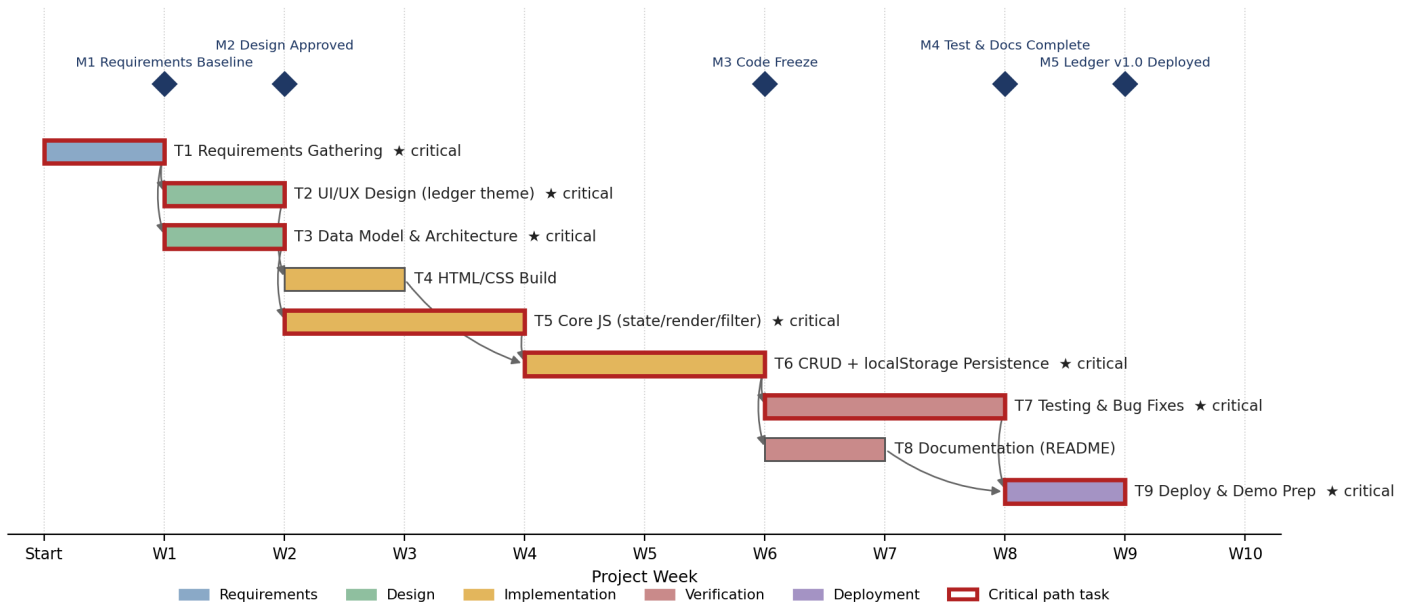

Deliverable 2. Phase Gates & Milestones

Phase	Wks	Entry Criteria	Exit Criteria	Sign-Off Artifact	Approver
Requirements	1	Team has reviewed the assignment brief and existing Ledger prototype	Feature list frozen (browse, search/filter, reserve, add, delete, persist)	Requirements & Feature List Doc	Team Lead
Design	2	Approved feature list	Ledger visual theme, layout, and event data schema finalized	Wireframes + Data Model Spec	UI/UX Lead & Team
Implementation	3–6	Approved wireframes and data model	HTML/CSS built; core JS (render/filter/search) and CRUD + localStorage complete; code frozen	Code Baseline (index.html, style.css, script.js)	Dev Leads
Verification	6–8	Frozen code baseline	Functional & cross-browser tests pass; README complete	Test Log + README	QA/Test Lead
Deployment & Maintenance	9	Passed testing; docs complete	Live on GitHub Pages; demo rehearsed	Deployed Repo + Demo Script	Whole Team

Milestones (zero-duration): M1 Requirements Baseline (end W1) · M2 Design Approved (end W2) · M3 Code Freeze (end W6) · M4 Test & Docs Complete (end W8) · M5 Ledger v1.0 Deployed (end W9).

Deliverable 3. Critical Path & Float

Task	Duration	Depends On	ES–EF	Float
T1 Requirements Gathering	1 wk	—	W1–W1	0 (critical)
T2 UI/UX Design	1 wk	T1	W2–W2	0 (critical)
T3 Data Model & Architecture	1 wk	T1	W2–W2	0 (critical)
T4 HTML/CSS Build	1 wk	T2	W3–W3	1 week
T5 Core JS (state/render/filter)	2 wk	T3	W3–W4	0 (critical)
T6 CRUD + localStorage Persistence	2 wk	T4, T5	W5–W6	0 (critical)
T7 Testing & Bug Fixes	2 wk	T6	W7–W8	0 (critical)
T8 Documentation (README)	1 wk	T6	W7–W7	1 week

Task	Duration	Depends On	ES–EF	Float
T9 Deploy & Demo Prep	1 wk	T7, T8	W9–W9	0 (critical)

Critical path: T1 → T2 → T5 → T6 → T7 → T9 (T3 also sits on a zero-float branch feeding T5). Total duration: **9 weeks**, with no slack anywhere on this chain — a slip on any of these tasks slips the whole project. **Float on non-critical tasks:** T4 (HTML/CSS Build) has **1 week of float** because it only needs to be ready before T6 starts, and T6 actually waits on the longer T5 branch; it could run in W3 or slip into W4 without affecting the deadline. T8 (Documentation) similarly has **1 week of float**, since T9 waits on the longer T7 (testing) branch, so documentation could be written in W7 or W8.

Deliverable 4. Risk Register (6 Entries)

ID	Risk	Likelihood	Impact	Severity	Owner	Mitigation / Contingency
R1	Scope creep — extra features added mid-build beyond the frozen MVP list	Medium	High	High	Team Lead	Freeze feature list at the Requirements gate; log new ideas for a v2 backlog instead of building them mid-sprint
R2	localStorage data loss or corruption (browser clears storage, malformed JSON)	Medium	Medium	Medium	Persistence Dev	try/catch already wraps storage calls; add a manual export/import (JSON download) as a backup option
R3	Team member unavailable during Implementation (exams, illness) — on critical path	Medium	High	High	Team Lead	Pair programming, shared code-decision notes, and cross-training so no module has a single point of failure
R4	Cross-browser inconsistencies (date input, localStorage quirks in Safari/Firefox)	Medium	Medium	Medium	QA/Test Lead	Test on 3+ browsers during Verification; reserve buffer time in T7 for browser-specific fixes
R5	Late integration between HTML/CSS and JS reveals mismatched element IDs/selectors	Low–Medium	Medium	Medium	Frontend Dev	Agree on a shared naming/ID convention at the Design gate, before Implementation starts
R6	GitHub Pages deployment issues (relative path or asset-loading errors)	Low	Medium	Low–Medium	Deployment Lead	Do a dry-run deployment during Implementation, not only in the final week
